



CITY OF  
**TOPEKA**



# Polk-Quincy Viaduct

Utility Relocation Project Update

# KDOT PQV West Project










# Background

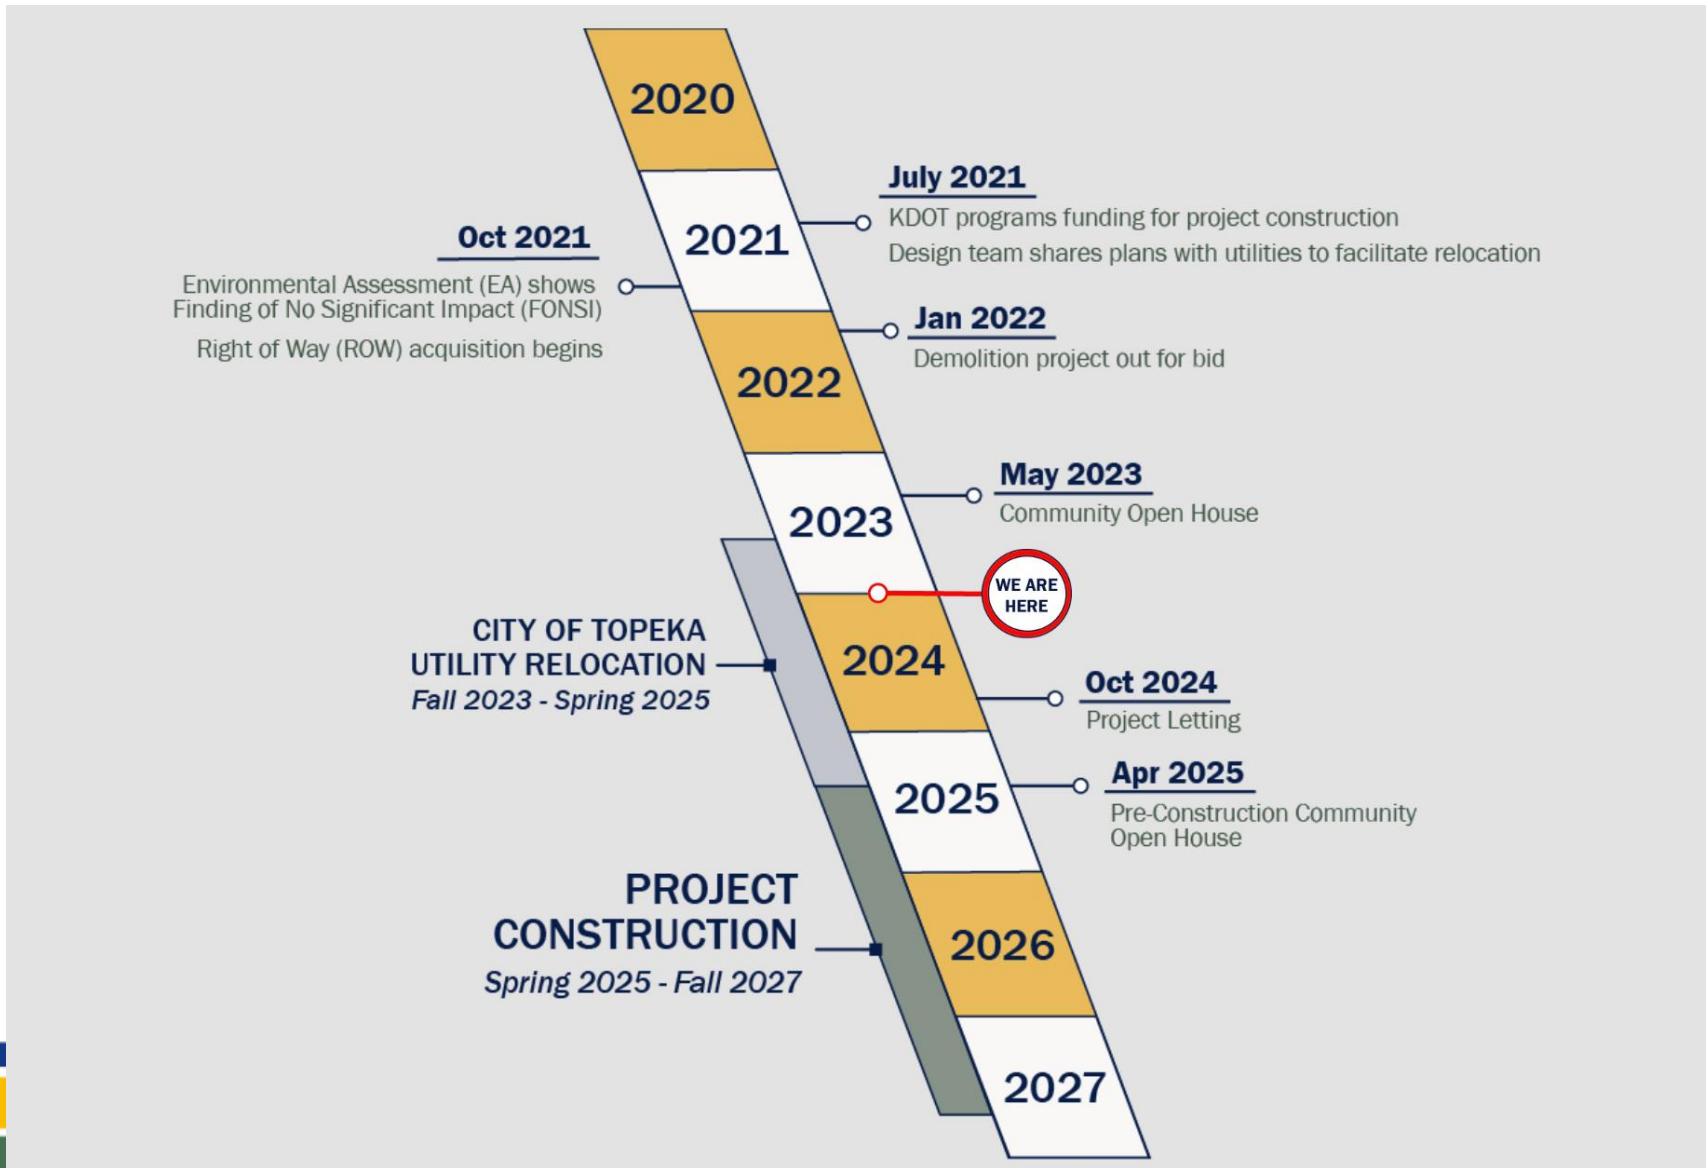

# City-Owned Utility Relocation

5

6,000'+ of water line

7,000'+ of sanitary sewer line

2,600'+ of storm sewer line


Storm sewer separation






# City Projects 2-7

-  New Storm Sewer
-  New Sanitary Sewer
-  New Water Line

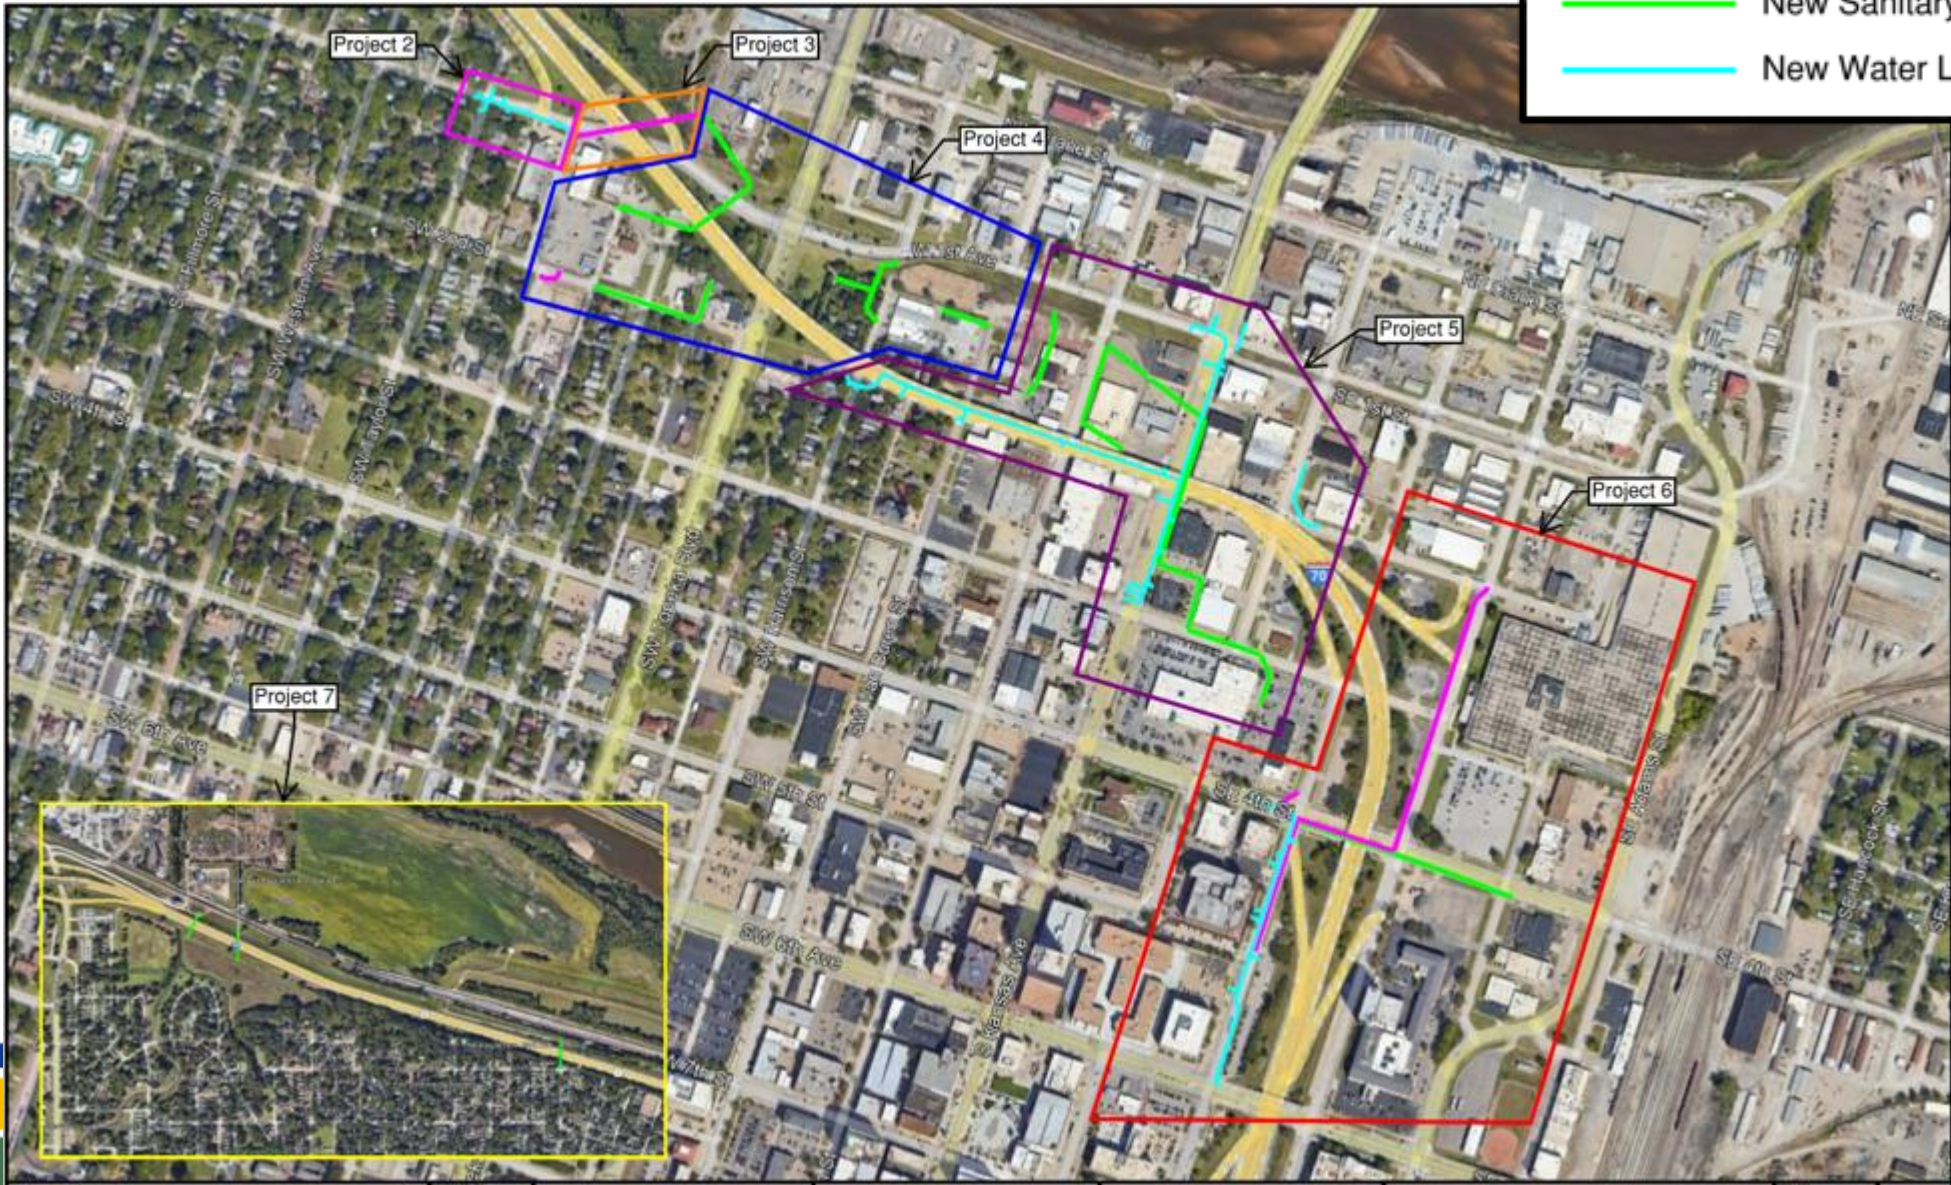



# Project 2

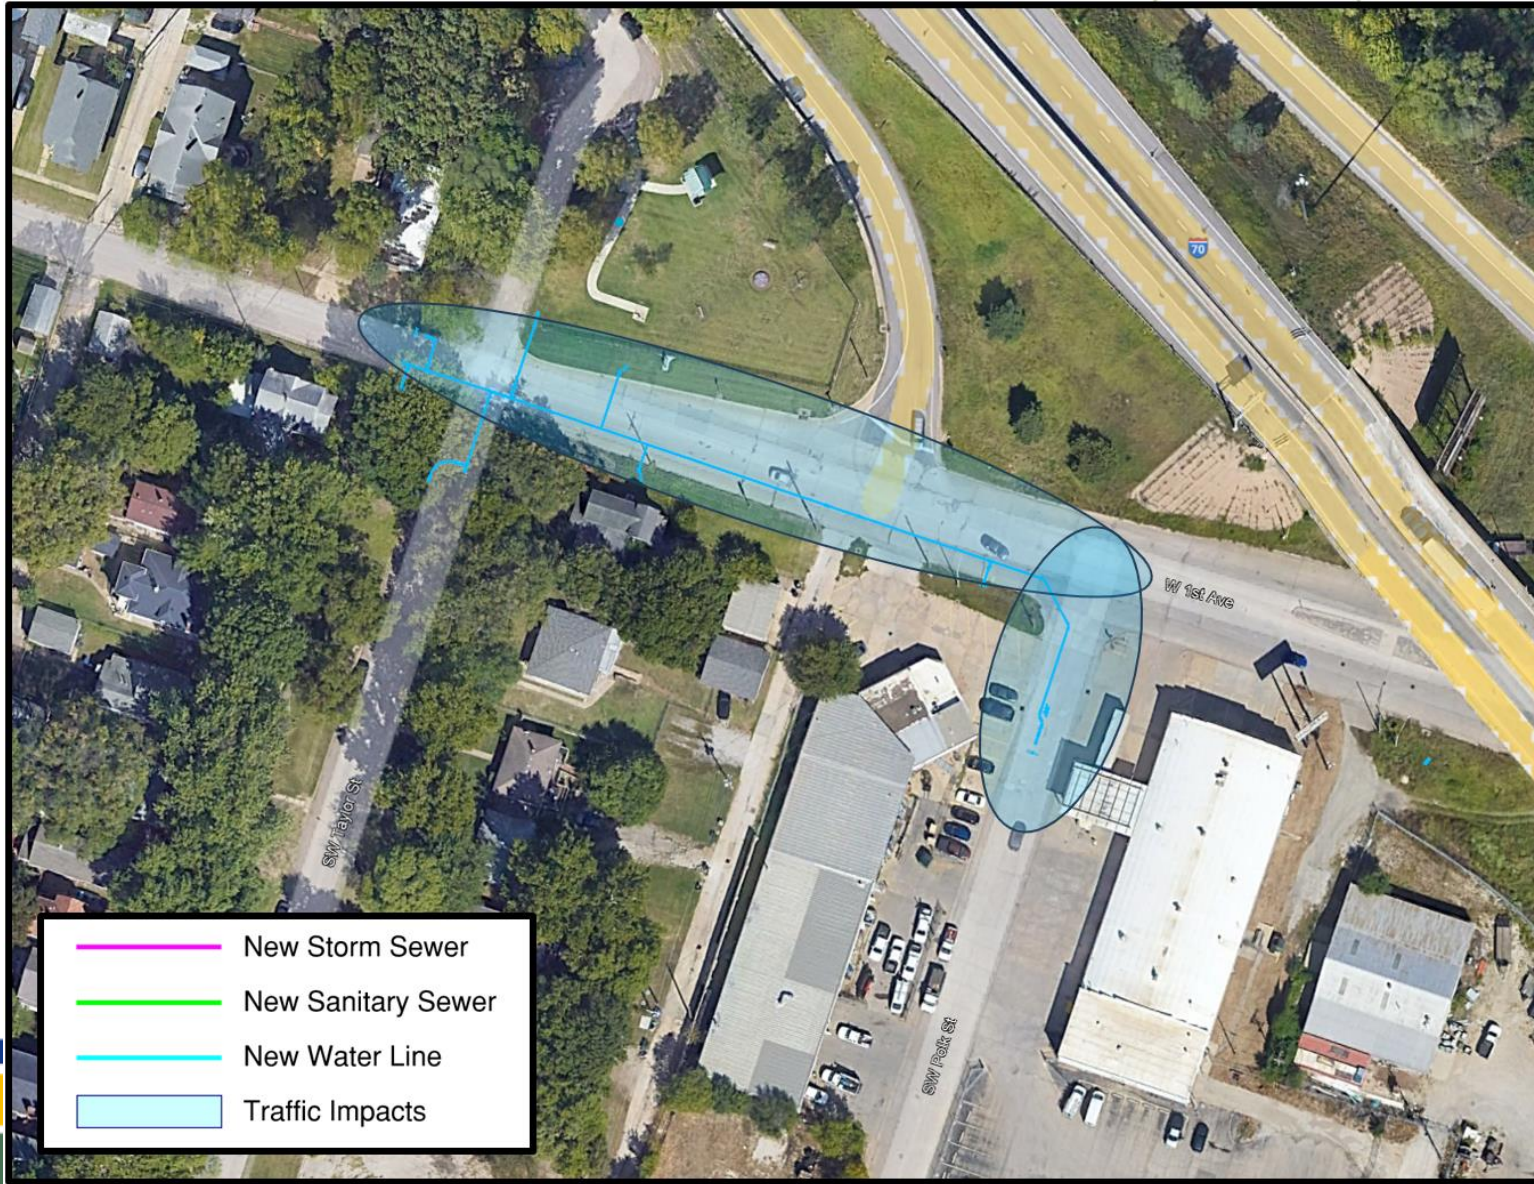


- Construction began in late 2023 and remains on schedule for completion in January 2024





# Project 3

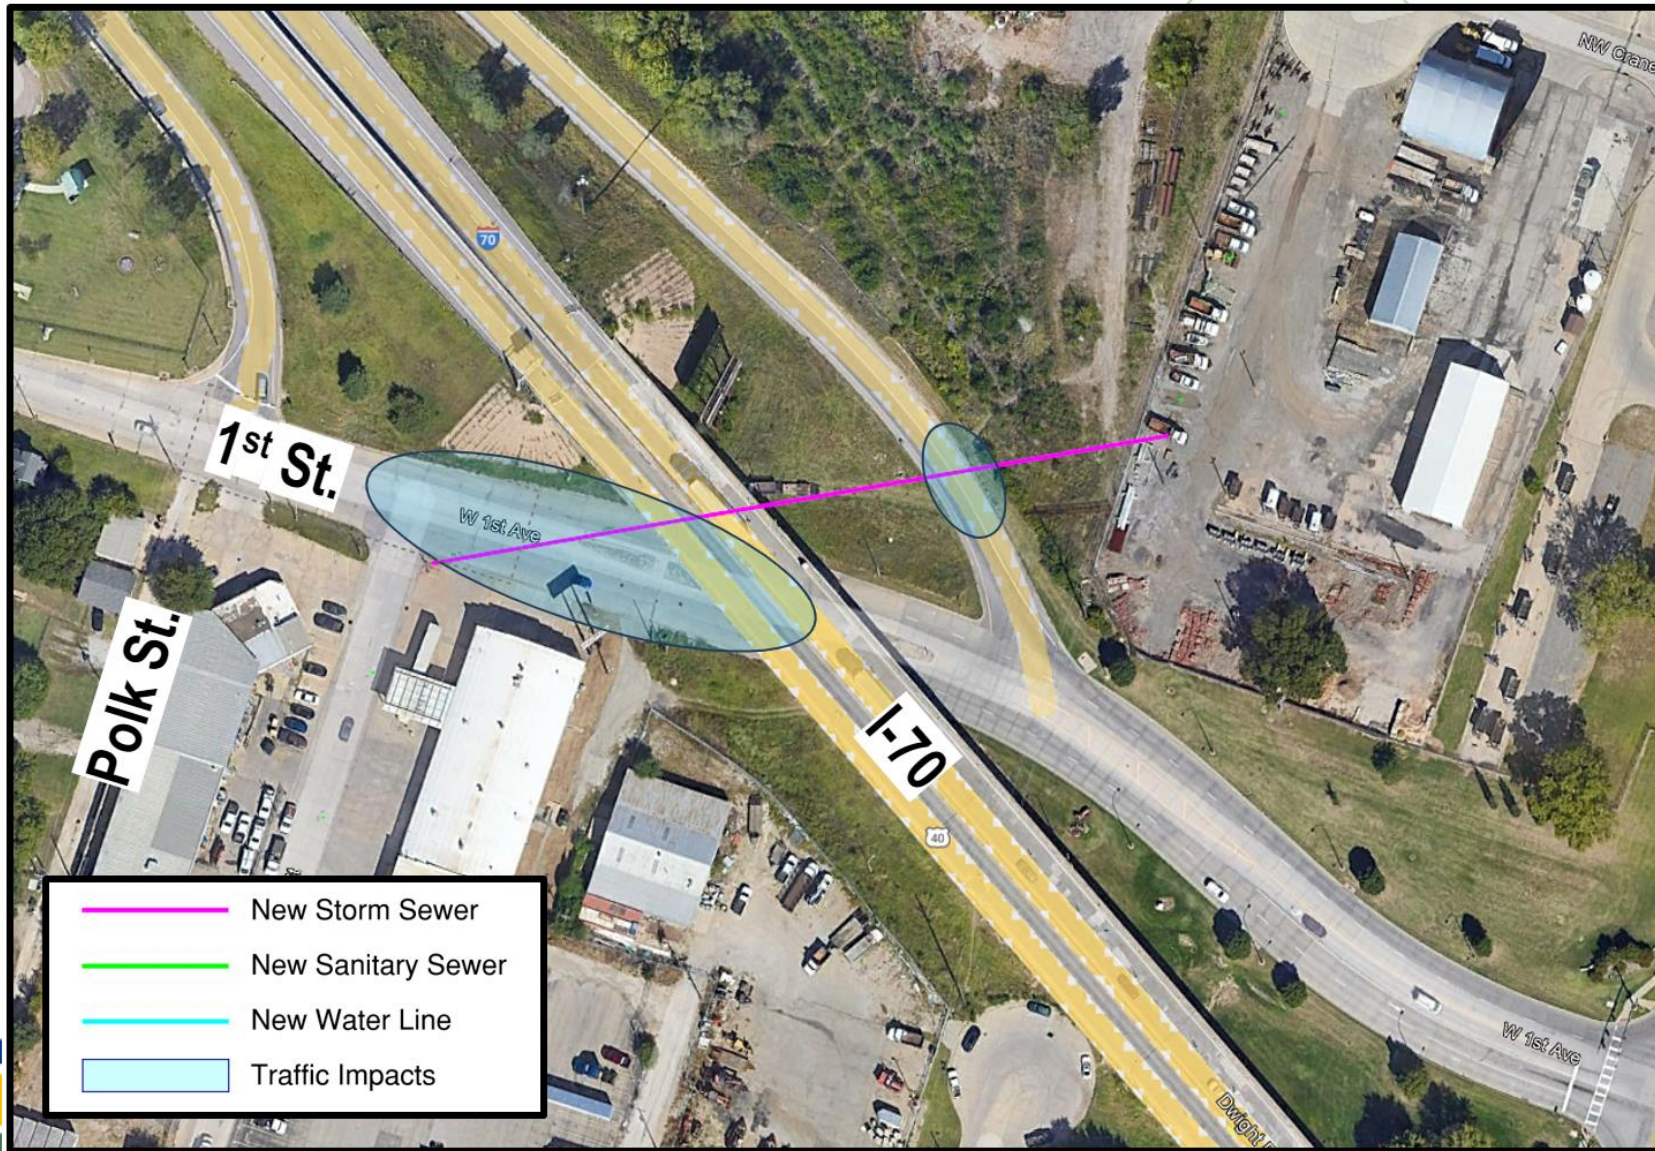


- Currently awarding bid
- Anticipated completion 11/15/2024.





# Project 4

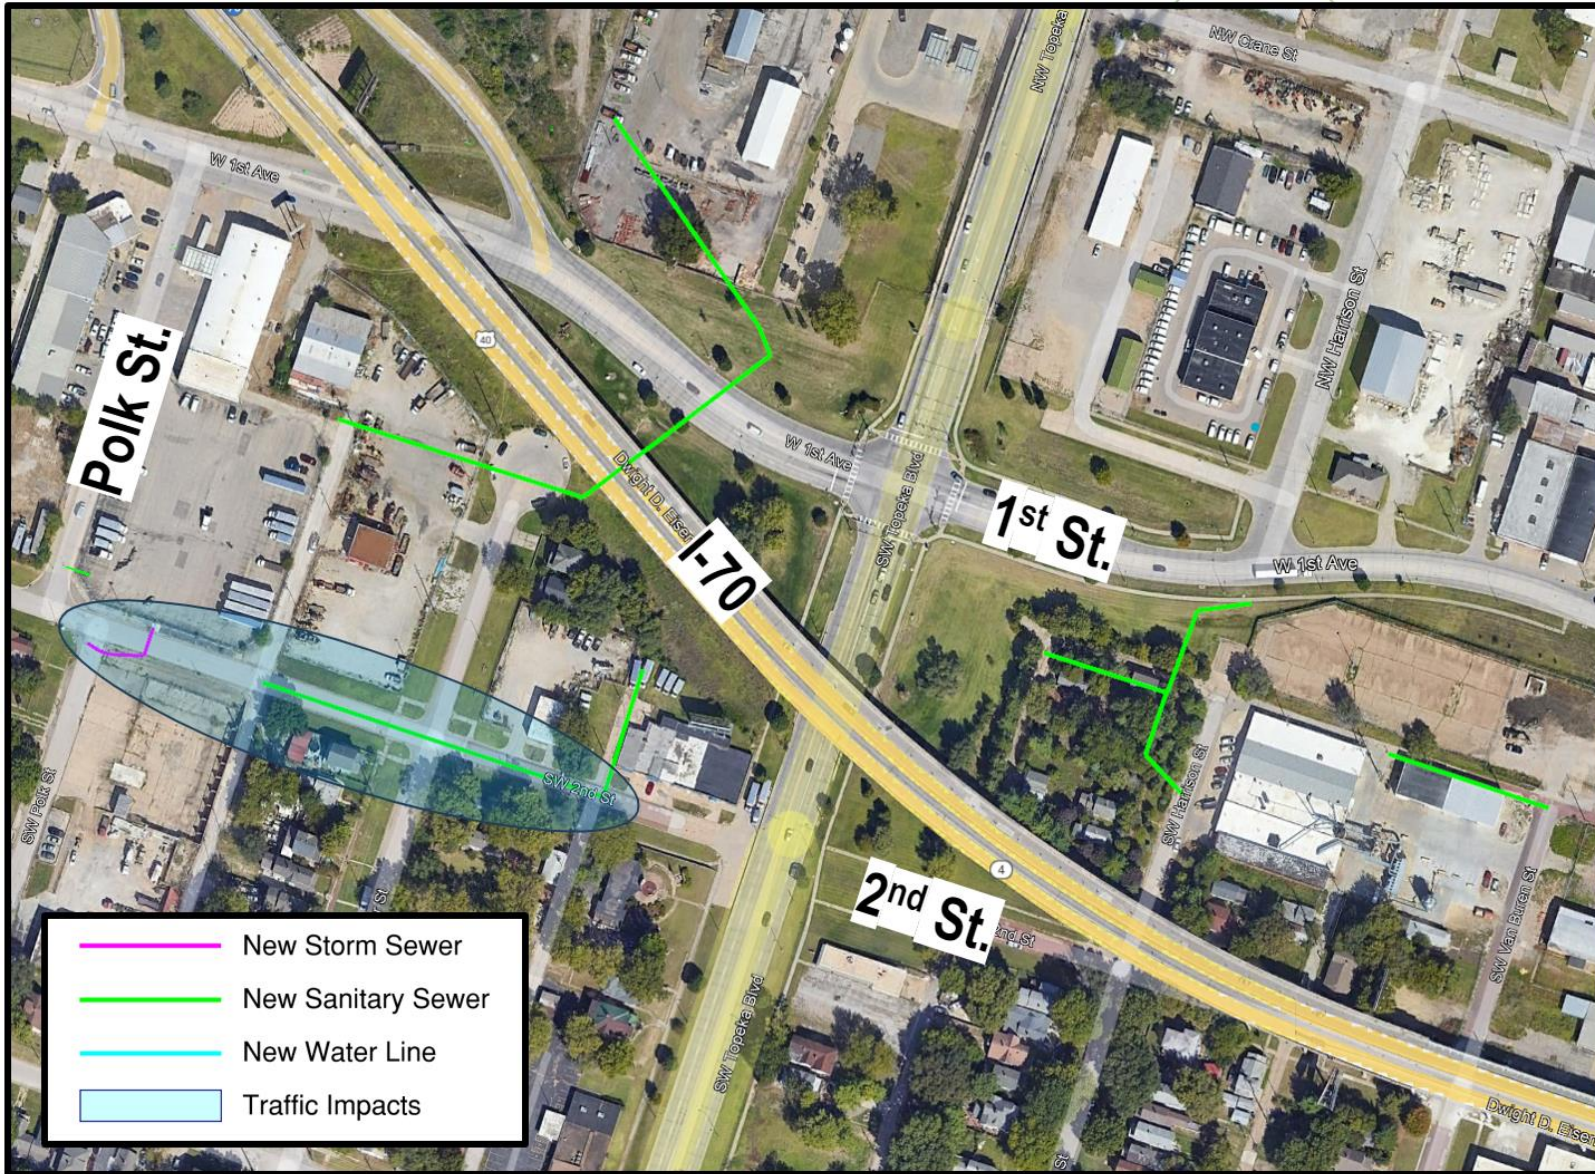


- Currently awarding bid
- Anticipated completion 1/31/2025





# Project 5

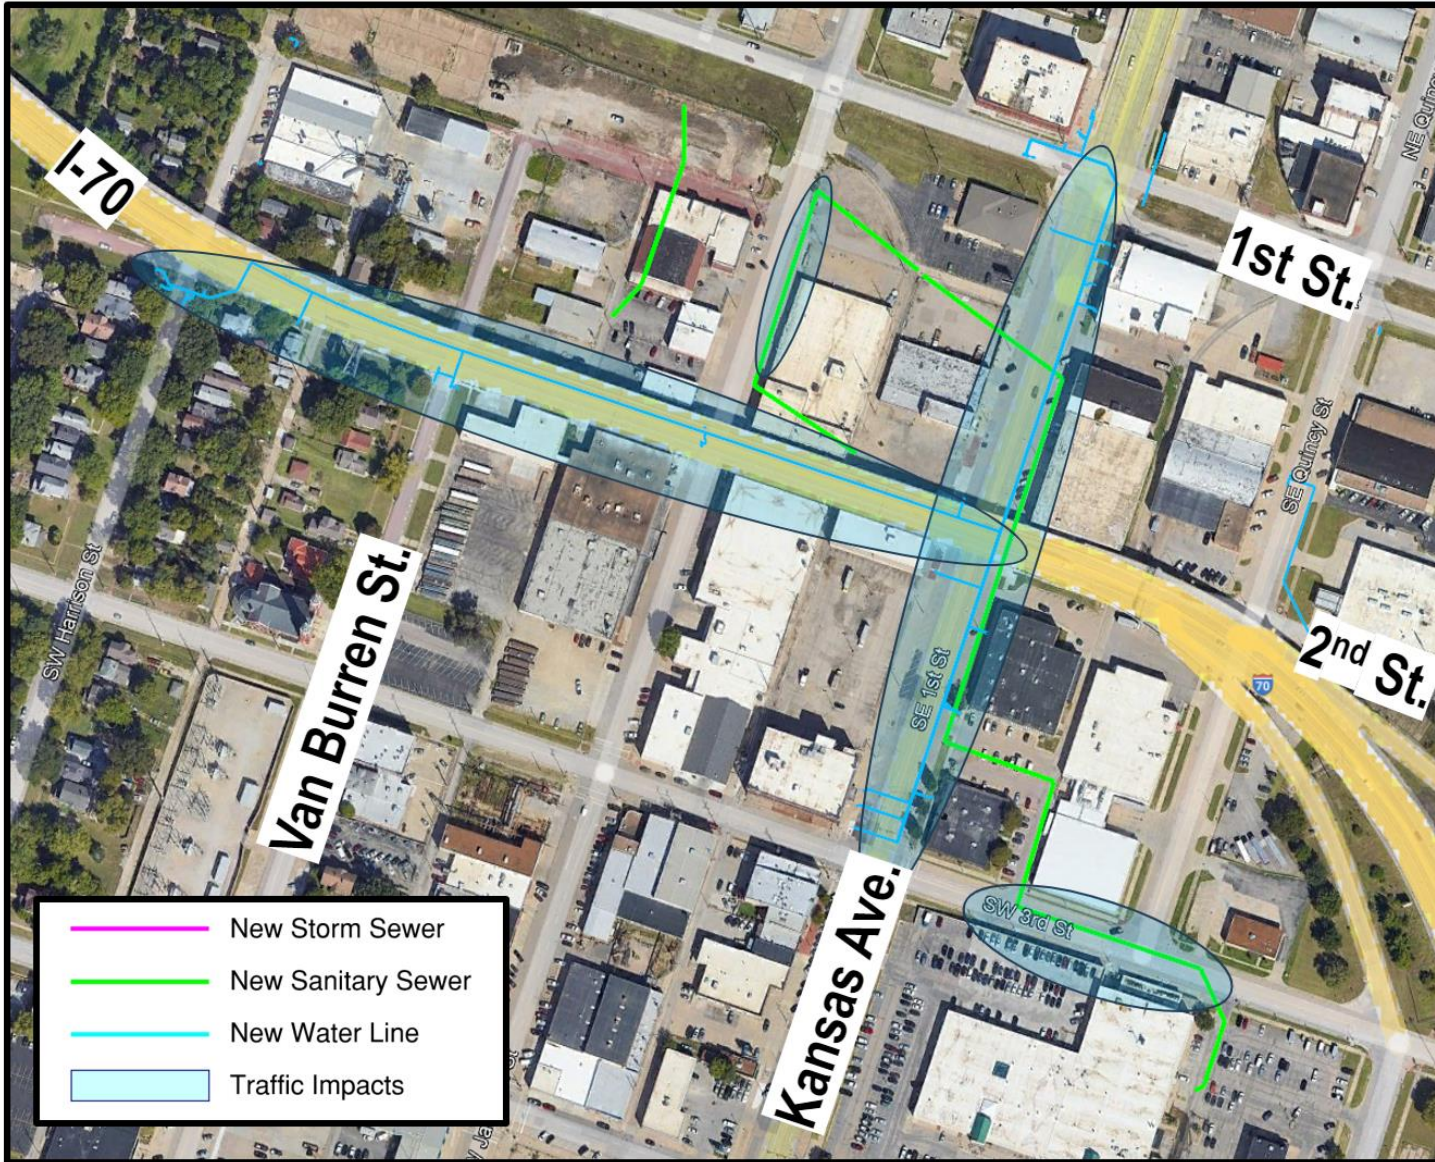


- Project awarded to Bettis
- Anticipated completion 1/31/2025





# Project 6

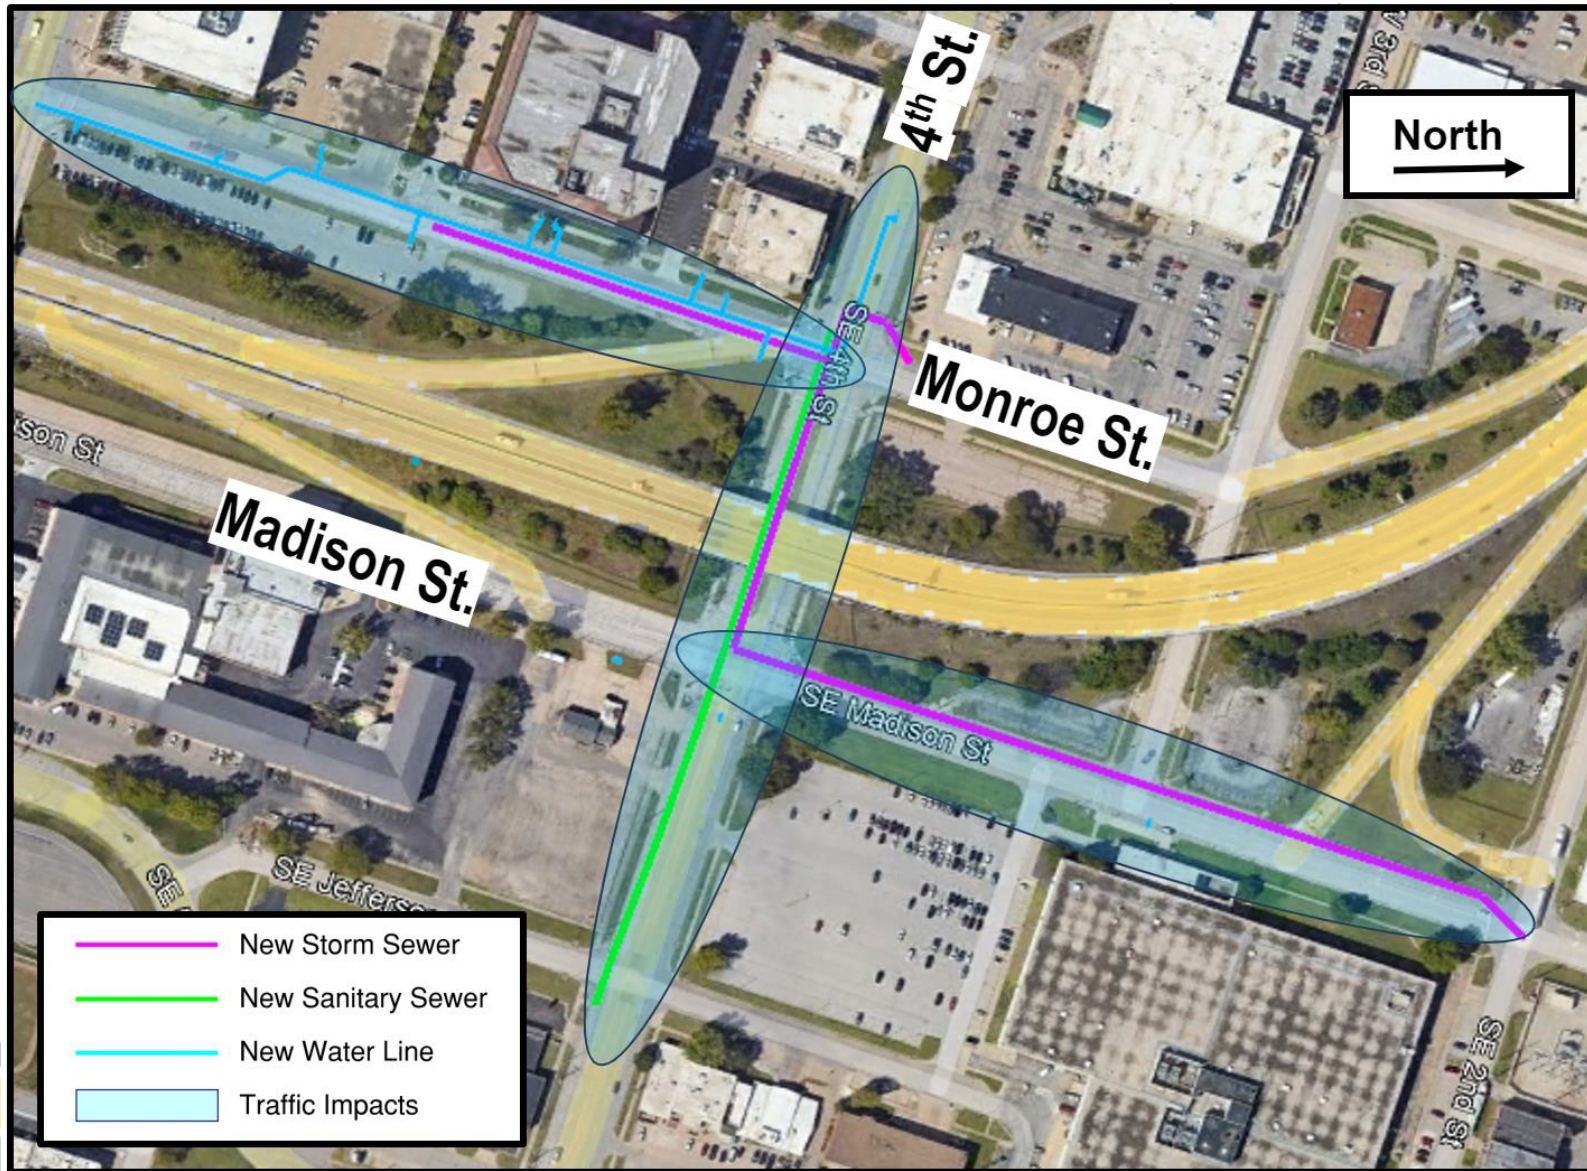

- Project awarded to EmCon Construction
- Anticipated completion 1/31/2025





# Project 7



- Project awarded to EmCon Construction
- Anticipated completion May 2024





# Budget

	<u>Engineering Estimate</u>	<u>Construction Cost</u>	<u>Difference</u>
Design, Inspection, Admin, Debt Issue	4,758,336	4,758,336	
Project 2	429,360	280,035	-35%
Project 3	1,833,538		
Project 4	4,495,934	4,396,780	-2%
Project 5	5,239,844	3,859,385	-26%
Project 6	4,170,089	2,946,836	-29%
Project 7	1,198,600	1,196,070	0%
<b>Total</b>	<b>\$ 22,125,700</b>	<b>\$ 17,437,442</b>	\$19,270,980*

\*w/ Eng Est for Proj # 3





- KDOT, KDHE, USACE and COT Departments
- Traffic control and impacts will be coordinated between all Utility and Public Works projects
- Traffic impacts will be coordinated with the Topeka Metro





# Ongoing Updates

---

For traffic control information and project updates:

**[Topeka.org/utilities/pqv](http://Topeka.org/utilities/pqv)**

For information on KDOT PQV West:

**[Polkquincy.org](http://Polkquincy.org)**

