

James Jackson, Topeka Public Works Director



## SW 10<sup>th</sup> – Wanamaker to Fairlawn



- The last section, SW Chatham to the middle of Fairlawn Road, is under demolition.
- The top lift (final 2 inches) will be placed from Fairlawn to west of Morna once this phase is complete.
- Final completion date: Nov. 19.





## SW 12<sup>th</sup> – Kansas to Washburn

- All but the top lift of asphalt is down between S Kansas and SW Topeka Blvd.;
  12-foot path being placed.
- Concrete street being placed between Topeka and Taylor St.
- Utility work 90% complete for 2021.
- The remaining subgrade is being worked to Washburn Ave.
- Completion date for the Kansas to Washburn section: Nov. 23.







## N Kansas Ave – Morse to Soldier St.




- The west half of Kansas and Morse intersection has been placed in addition to the base courses of asphalt to just north of St. John Street.
- Work continues on the west side of the street (southbound lane).
- Project completion date: Dec. 2.





# SE Deer Creek Trfy – I-70 to SE 6<sup>th</sup> Ave.

- Concrete pavement patching nearly complete in southbound lanes.
- The completion date is anticipated to be mid/late October.
- Two-way traffic has been maintained at all times.

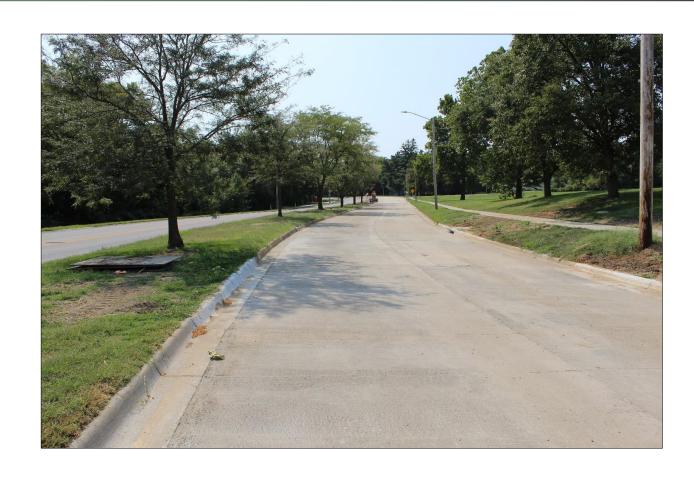





# Central Park Neighborhood SORT



- The remaining sanitary sewer main and alley are under construction.
- Completion date: Oct. 29.





# SE 37<sup>th</sup> – Turnpike Bridge to SE California



- The eastbound lane is open to westbound traffic only.
- The westbound lane has been milled and about a third of the curb and gutter has been removed.
- Curb/gutter to be placed this week.
- Full depth patches and overlay to follow.
- Final completion: Late October.





# NW Furman Road – Lower Silver Lake Road to ¼ mile north



- Demolition of existing asphalt surface and subgrade work continues.
- Final Completion: Nov. 8





#### SE 29<sup>th</sup> & Kansas Intersection



- Construction is expected to begin this week.
- Most of the north leg will be replaced; the raised median will be removed and the turn lane will be striped.
- The middle of the intersection will be milled and overlaid.
- Final Completion Nov. 5





#### SE Adams – 37<sup>th</sup> to 45<sup>th</sup>



- SE Adams St. 37<sup>th</sup> to 45<sup>th</sup> mill and overlay originally scheduled for 2022.
- This will be constructed in 2021.
- Adams will be the detour route for the SE California Project in 2022.
- Mill and overlays on SW 45th St. and SW 29th are being added to the 2022 project list in its place.
- Start: Oct. 4
- Final Completion: Oct. 29





## SW Fillmore and SW 9<sup>th</sup> Street



- SW Fillmore and SW 9<sup>th</sup> St.
- Mill and overlays
- Start: Oct. 10
- Final completion: Oct. 29





# In Design 17th/Wanamaker/Westport/Bridge



- Both 17<sup>th</sup> I-470 Bridge to Wanamaker, and Westport Dr. – 17<sup>th</sup> to Wanamaker will be reconstructed in 2022 prior to the start of the SW 17<sup>th</sup> – MacVicar to I-470 Bridge Project in 2023 and 2024.
- Waterline replacement from Westport to the Days Inn and Econo Lodge hotels.
- Bids in the spring.





# In Design SE California – 37<sup>th</sup> to 45<sup>th</sup>



- Reconstruct SE California from a twolane rural section to a three-lane section with curb & gutter.
- Completes street repairs, road rehabilitation, and complete reconstruction from I-70 on the north to SW 45th on the south.
- Bids in the spring.





## In Design 17<sup>th</sup> – MacVicar to I-470



- Public engagement and outreach planning and preparations underway.
- Public Outreach will be scheduled to business owners, City staff and elected officials, and neighborhood leaders this fall.
- Construction: 2023 and 2024.





Thank you. Questions?

